INSPECTION REPORT



For the Property at:

123 SAMPLE STREET

BAY AREA, MD

Prepared for: SAMPLE INSPECTION

Inspection Date: Monday, September 1, 2014

Prepared by: Bobby Davidson

HomePro Home Inspections

Home Pro 324 Kidwell Ave. Centreville, MD 21617 443 871 7523

www.homeprobayarea.com Robert.g.davidson@gmail.com

HomePro Home Inspections

INVOICE

December 22, 2014

Client: Sample Inspection

Report No. 1011 For inspection at: 123 Sample Street Bay Area, MD

on: Monday, September 1, 2014

Home inspection \$400.00

Total \$400.00

PAID IN FULL - THANK YOU!

123 Sample Street, Bay Area, MD September 1, 2014

SUMMARY

ROOFING **EXTERIOR** STRUCTURE

HEATING

COOLING

INSULATION

PLUMBING

www.homeprobayarea.com

INTERIOR

This Summary outlines potentially significant issues from a cost or safety standpoint. This section is provided as a courtesy and cannot be considered a substitute for reading the entire report. Please read the complete document.

Priority Maintenance Items

Roofing

SLOPED ROOFING \ Asphalt shingles

Condition: • Missing, loose or torn

Implication(s): Chance of water damage to contents, finishes and/or structure

Location: Various Task: Repair or replace

Time: Immediate Cost: Major

Electrical

DISTRIBUTION SYSTEM \ Smoke detectors

Condition: • Missing Location: Bedroom Task: Upgrade Time: Immediate

Cooling & Heat Pump

General

• Very dirty filter in air handler is restricting airflow.

Location: Crawl Space

Task: Replace Time: Immediate

Interior

BASEMENT \ Wet basement - evidence

Condition: • Water on floor

Implication(s): Chance of water damage to contents, finishes and/or structure

Location: Basement Task: further evaluation

This concludes the Summary section.

The remainder of the report describes each of the home's systems and also details any recommendations we have for improvements. Limitations that restricted our inspection are included as well.

The suggested time frames for completing recommendations are based on the limited information available during a pre-purchase home inspection. These may have to be adjusted based on the findings of specialists.

123 Sample Street, Bay Area, MD

Report No. 1011 **SUMMARY**

September 1, 2014

SUMMARY ROOFING EXTERIOR STRUCTURE HEATING COOLING INSULATION PLUMBING INTERIOR Home Improvement - ballpark costs Page 2 of 19 Providing great home inspections for every client every time

123 Sample Street, Bay Area, MD September 1, 2014 www.homeprobayarea.com

SUMMARY ROOFING EXTERIOR STRUCTURE ELECTRICAL HEATING COOLING INSULATION PLUMBING INTERIOR

Description

General: • house



1.

Sloped roofing material: • <u>Asphalt shingles</u>

Sloped roof flashing material: • Copper

Probability of leakage: • High

Limitations

Inspection performed: • By walking on roof

Recommendations

SLOPED ROOFING \ Asphalt shingles

1. Condition: • Near end of life expectancy

Implication(s): Chance of water damage to contents, finishes and/or structure

2. Condition: • Missing, loose or torn

Implication(s): Chance of water damage to contents, finishes and/or structure

Location: Various

Task: Repair or replace

Time: Immediate **Cost**: Major

123 Sample Street, Bay Area, MD

Report No. 1011

COOLING INSULATION PLUMBING SUMMARY STRUCTURE HEATING ROOFING

September 1, 2014

2. Missing, loose or torn

Report No. 1011 **EXTERIOR**

123 Sample Street, Bay Area, MD

EXTERIOR

September 1, 2014

www.homeprobayarea.com

SUMMARY

ROOFING

STRUCTURE

PLUMBING

Description

Gutter & downspout material: • Aluminum

Gutter & downspout discharge: • Below grade • Above grade

Lot slope: • Away from building Wall surfaces - masonry: • Brick

Wall surfaces: • Metal siding

Driveway: • Asphalt Porch: • Concrete

Exterior steps: • Wood • Brick

Garage: General

Detached 2 car garage with brick veneer.

Limitations

Exterior inspected from: • Ground level

Recommendations

ROOF DRAINAGE \ Downspouts

3. Condition: • Loose connections

Implication(s): Leakage

Location: Rear Task: Repair Cost: Minor




3. Loose connections

4. Condition: • Downspouts end too close to building

Implication(s): Chance of water damage to contents, finishes and/or structure

123 Sample Street, Bay Area, MD September 1, 2014 SUMMARY ROOFING **EXTERIOR** PLUMBING

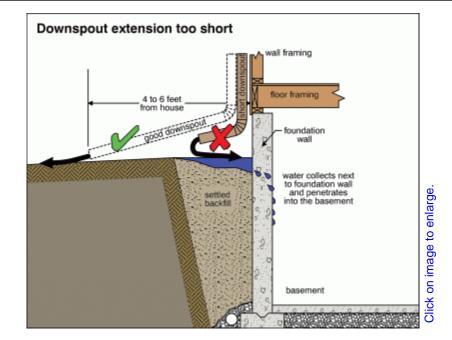

WALLS \ Brick, stone and concrete

5. Condition: • Mortar deterioration

rake and point

Implication(s): Chance of water entering building | Weakened structure | Chance of structural movement

Location: Front First Floor

Task: Repair



4. *Mortar deterioration*

PORCHES, DECKS, STEPS, PATIOS AND BALCONIES \ Floors

6. Condition: • Paint or stain needed

Implication(s): Cosmetic defects | Shortened life expectancy of material

Location: Rear Porch

Task: Protect Cost: Minor

SUMMARY ROOFING EXTERIOR STRUCTURE ELECTRICAL HEATING COOLING INSULATION PLUMBING INTERIOR

September 1, 2014



5. Paint or stain needed

STRUCTURE Report No. 1011

123 Sample Street, Bay Area, MD September 1, 2014 www.homeprobayarea.com

SUMMARY ROOFING EXTERIOR STRUCTURE ELECTRICAL HEATING COOLING INSULATION PLUMBING INTERIOR

Description

Configuration: • Basement • Crawl space

Floor construction: • <u>Joists</u> • Subfloor - plank

Exterior wall construction: • <u>Wood frame, brick veneer</u> • <u>Masonry</u>
Roof and ceiling framing: • <u>Rafters/roof joists</u> • <u>Plank sheathing</u>

Limitations

Attic/roof space: • Entered but access was limited

Percent of foundation not visible: • 20 %

Recommendations

FOUNDATIONS \ Foundation

7. Condition: • Typical minor cracks

Implication(s): Chance of water entering building

Time: Less than 5 years

FLOORS \ Joists

8. Condition: • Sag or springy

Implication(s): Chance of structural movement | Bouncy, springy floors

Task: Monitor

123 Sample Street, Bay Area, MD September 1, 2014 SUMMARY ROOFING

Description

General: • manual generator transfer switch and generator receptical installed



Service entrance cable and location: • Underground aluminum

Service size: • 200 Amps (240 Volts)

Main disconnect/service box rating: • 200 Amps

Main disconnect/service box type and location: • Breakers - basement

System grounding material and type: • Copper - water pipe and ground rod

Auxiliary panel (subpanel) rating: • 60 Amps

Distribution wire material and type: • Copper - non-metallic sheathed • Aluminum - non-metallic sheathed

Type and number of outlets (receptacles): • Grounded - typical

Circuit interrupters: Ground Fault (GFCI) & Arc Fault (AFCI):

No GFCI

up stairs hall bath

- GFCI bathroom
- GFCI outside
- GFCI kitchen

Smoke detectors: • Present

Limitations

System ground: • Continuity not verified

September 1, 2014

Report No. 1011

SUMMARY ROOFING STRUCTURE

Recommendations

123 Sample Street, Bay Area, MD

DISTRIBUTION SYSTEM \ Outlets (receptacles)

9. Condition: • Loose front exterior receptical open to weather

Location: Front Task: Repair Cost: Minor

10. Condition: • No GFI (Ground Fault Interrupter)

Implication(s): Electric shock

Location: Exterior Task: Upgrade Cost: Minor

DISTRIBUTION SYSTEM \ Cover plates

11. Condition: • Damaged Implication(s): Electric shock

Location: Rear porch

Task: Replace Cost: Minor



7. Damaged

DISTRIBUTION SYSTEM \ Smoke detectors

12. Condition: • Missing Location: Bedroom Task: Upgrade Time: Immediate

123 Sample Street, Bay Area, MD September 1, 2014

SUMMARY ROOFING STRUCTURE HEATING

Description

System type:

• Boiler



8. Boiler

Boiler manufacturer: • Olsen Heat distribution: • Baseboards

Approximate capacity: • 120,000 BTU/hr

Efficiency: • Conventional

Approximate age: • 35 years • Near end of life expectancy

Fireplace: • Wood-burning fireplace

Recommendations

OIL HOT WATER BOILER \ Life expectancy

13. Condition: • Near end of life expectancy

various rust and signs of age.

Implication(s): Equipment failure | No heat for building

Task: Further evaluation

COOLING & HEAT PUMP

Report No. 1011

123 Sample Street, Bay Area, MD September 1, 2014 www.homeprobayarea.com

SUMMARY

ROOFING

STRUCTURE

COOLING

Description

Air conditioning type: • Evaporative cooler

Manufacturer: • Goodman

Compressor approximate age: • 3 years

Failure probability: • Low

Recommendations

General

14. • Very dirty filter in air handler is restricting airflow.

Location: Crawl Space

Task: Replace Time: Immediate

INSULATION AND VENTILATION

Report No. 1011

www.homeprobayarea.com

123 Sample Street, Bay Area, MD September 1, 2014 SUMMARY ROOFING INSULATION

Recommendations

ATTIC/ROOF \ Insulation


15. Condition: • Gaps or voids

Implication(s): Increased heating and cooling costs | Reduced comfort

Location: Attic Task: Improve Cost: Minor

16. Condition: • Covering recessed lights Implication(s): Increased fire hazard

Location: Attic Task: Correct Time: Immediate Cost: Minor

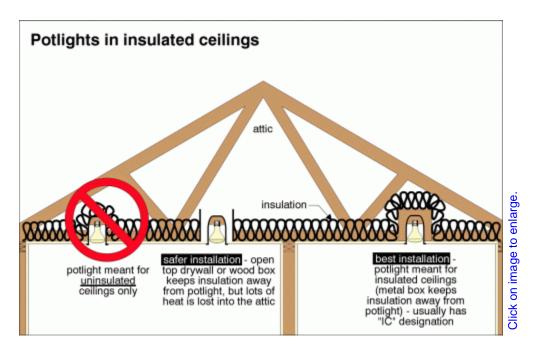

PLUMBING Report No. 1011

123 Sample Street, Bay Area, MD September 1, 2014 www.homeprobayarea.com

SUMMARY ROOFING EXTERIOR STRUCTURE ELECTRICAL HEATING COOLING INSULATION PLUMBING INTERIOR

Description

Water supply source: • Private

Service piping into building: • Plastic

Supply piping in building: • Plastic • Galvanized steel

Main water shut off valve at the: • Basement

Water flow and pressure: • Functional

Water heater fuel/energy source:

• <u>Oil</u>

Integral boiler heats water

Water heater type: • Tankless/indirect

Waste piping in building: • Plastic • Galvanized steel

Pumps: • Sump pump

Recommendations

General

17. • caulk or grout matter shower tile

Location: Master Bathroom

Task: Repair Cost: Minor



9.

FIXTURES AND FAUCETS \ Toilet

18. Condition: • Loose

Implication(s): Chance of water damage to contents, finishes and/or structure | Sewage entering the building


Location: Bathroom Master Bedroom

Task: Repair Time: Immediate

123 Sample Street, Bay Area, MD September 1, 2014 www.homeprobayarea.com

SUMMARY ROOFING **PLUMBING**

Cost: Minor

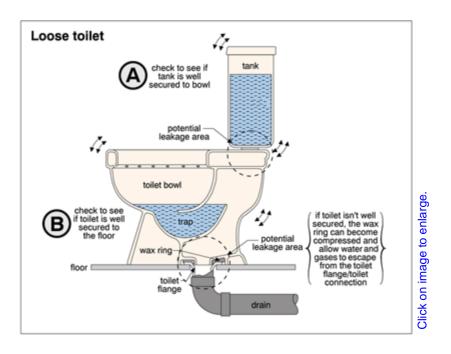

19. Condition: • Running continuously

Implication(s): Chance of condensation damage to finishes and/or structure | Increased water consumption

Location: Half Bathroom

Task: Repair Cost: Minor

INTERIOR Report No. 1011

123 Sample Street, Bay Area, MD September 1, 2014 www.homeprobayarea.com

SUMMARY ROOFING EXTERIOR STRUCTURE ELECTRICAL HEATING COOLING INSULATION PLUMBING INTERIOR

Description

Major floor finishes: • <u>Hardwood</u> • <u>Ceramic</u>

Major wall and ceiling finishes: • Plaster/drywall

Windows:

- Single/double hung
- Wood

original and replacements

Glazing:

• Single

originals

• Double

replacements

Exterior doors - type/material: • Hinged • Solid wood

Range fuel: • Electricity

Appliances: • Refrigerator • Dishwasher • Microwave oven • Door bell **Laundry facilities:** • Washer • Laundry tub • Dryer • 240-Volt outlet

Limitations

Not included as part of a building inspection: • Security systems and intercoms

Recommendations

FLOORS \ Ceramic tile, stone, marble, etc

20. Condition: • Grout missing

Implication(s): Cosmetic defects | Trip or fall hazard

Location: Second Floor Hallway Bathroom

Task: Repair Cost: Minor

123 Sample Street, Bay Area, MD September 1, 2014

SUMMARY ROOFING STRUCTURE ELECTRICAL INTERIOR



10. Grout missing

WINDOWS \ Glass (glazing)

21. Condition: • Missing

Implication(s): Cosmetic defects | Chance of water entering building | Increased heating and cooling costs | Reduced

comfort

Location: Front Second Floor Hall

Task: Repair



11. Missing

DOORS \ Doors and frames

22. Condition: • Racked/out-of-square

Implication(s): Cosmetic defects | Chance of damage to finishes and structure


Location: Second Floor Bathroom Hallway Bathroom

Task: Repair

Time: Discretionary

Cost: Minor

123 Sample Street, Bay Area, MD September 1, 2014 SUMMARY ROOFING INTERIOR

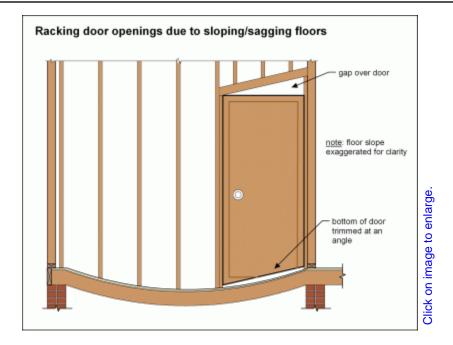


BASEMENT \ Wet basement - evidence

23. Condition: • Water on floor

Implication(s): Chance of water damage to contents, finishes and/or structure

Location: Basement Task: further evaluation

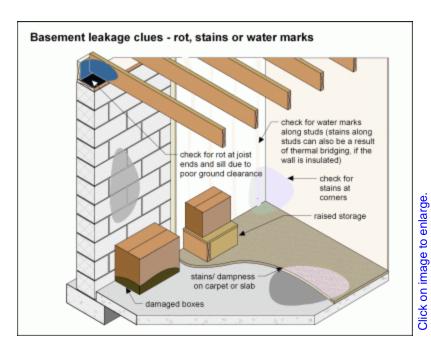

123 Sample Street, Bay Area, MD

Report No. 1011 **INTERIOR**

September 1, 2014

ROOFING COOLING INSULATION PLUMBING SUMMARY STRUCTURE ELECTRICAL HEATING INTERIOR



12. Water on floor

END OF REPORT
